

HXVP STUDIO V2 – PRODUCT REQUIREMENTS DOCUMENT

FIELD	VALUE
Version	0.3 (timeline compressed + user-flow inventory added)
DRI	Jerry Zheng
Stakeholders	Director (boss) · Original engineer (legacy context) · yinadong-design (design partner)
Last updated	2026-05-28
Status	● Draft v0.3 · pending director sign-off on §12 (User Flows) before any further build
Key dates	6/15 internal milestone · early July production launch
Demo URL	https://jerry6063.github.io/HXVP-v2-demo/
Private repo	https://github.com/Jerry6063/HXVP-v2 (branch: <code>v2-redesign</code>)
Public demo repo (MIT)	https://github.com/Jerry6063/HXVP-v2-demo

READING GUIDE

Boss / non-tech reviewers: read §1, §3, §5, §11 only (≈ 5 min). **Engineers / designers:** read everything plus appendices. **Discussion:** leave comments on the exported Google Doc; the canonical version lives in git.

Part I – Strategic Overview (for Boss)

1. TL;DR

HXVP Studio v2 is a **focus refinement** of the existing studio operations portal. v1 (the version built by the previous engineer in collaboration with the director) is functionally complete but, per the director's 2026-05-28 review, feels unfocused, complex, and feature-bloated. v2 preserves the **4-portal architecture** (Production · Client · Talent · Crew) the director affirms is core to the workflow, but aggressively narrows each portal's purpose.

One sentence: *Fewer features, clearer paths, faster comprehension.*

TIMELINE (COMPRESSED)

MILESTONE	DATE	SCOPE
Sprint 0 	done by 5/28	Visual baseline + Apple-style transitions + Production Dashboard Status Board + public demo
Sprint 0.5	5/29 → 6/4	Model-merge revert (4 portals restored) · Feature audit with director · User-flow sign-off (\$12)
Sprint 1 — 6/15 Internal Milestone	6/5 → 6/15	All 4 portals' landing pages reflect "the one job" sentence · 全球 global search · Tier-3 features hidden · demo to boss
Sprint 2 — Early-July Launch	6/16 → 7/6	Top user flows (\$12) work end-to-end with v2 UI · Talent/Crew mobile-friendly · Activity Feed wired to real data · backend hookup if applicable · bug squash
Post-launch (v1.5)	7/7 onward	Remaining ~50 deep detail pages · Shoot Command Center · Cascade prompts · Bulk operations

WHY THIS VERSION (V0.3) EXISTS

Two changes since v0.2:

- Boss confirmed deadlines: 6/15 (internal milestone) + early July (launch).** The previous 6-sprint plan ending 8/10 was too loose. Reduced to **2 sprints + a 0.5 prep week**.
- Boss directive:** "重点是 *user flow* 和 *workflow*,要列出来现在的让 *boss* 看看是不是对的。" — Section §12 below is the single most important deliverable of this week. **No further build proceeds until §12 flows are signed off.**

2. BACKGROUND

What was inherited	Full-stack platform: React 19 + Vite + Django REST + PostgreSQL, deployed on Render. ~74 frontend files, ~26 700 LOC, 55 po
Built by	Previous engineer in collaboration with the director (boss). Functionally complete, in production at <code>hxvp-studio-frontend.onrer</code>
Why v2 now	Director took the system to feature-completeness, then handed it to current owner (Jerry) for usability and quality polish.
2026-05-28 director review	Director reviewed v1 (main branch) and reaffirmed the 4-portal structure as core. Critique: "重点不突出 / 看起来很复杂 / 有些功能
Constraint from boss	"Don't break what works" + "Keep all 4 portals" + "Cut the fat."

3. PROBLEM STATEMENT

Director's verbatim feedback (2026-05-28, on v1 main):

- 重点不突出 — "The focus / what's important isn't obvious."
- 看起来很复杂 — "It looks complex."
- 有些功能不是必要 — "Some features aren't necessary."

Reinterpretation — three distinct problems hiding behind one complaint:

#	DIRECTOR'S WORD	CONCRETE PAIN	HYPOTHESIS
P1	重点不突出	After login, the user can't tell what THE most important thing on this screen is	Dashboard treats all KPIs/lists as equal-weight; no visual hierarchy
P2	看起来很复杂	Sidebar with 10+ flat items, pages with 5+ tabs, modals nested in modals	No progressive disclosure; everything visible at all times
P3	有些功能不是必要	~20–30 % of features are likely rarely used but always visible	No usage data; feature audit never performed

These three together cause one user feeling: "I don't know where to start, and I'm overwhelmed."

! **Open question for Boss:** of P1 / P2 / P3, which is most important to address first? (My recommendation: P1, because it's a 1-week visual hierarchy fix, not a feature-deprecation political minefield.)

4. USERS & JOBS TO BE DONE

Per director affirmation, the 4-portal architecture is preserved. Each portal has its own persona and its own primary job:

PORTAL	PERSONA	THE ONE JOB (PROPOSED — NEEDS DIRECTOR CONFIRMATION)	DAILY USAGE
Production	Studio admin / boss	"See what's blocking today and unblock it."	Multiple times daily
Client	Brand / agency contact	"Check my project and approve what needs approving."	Weekly bursts
Talent	Cast, model, actor	"Accept bookings, read call sheets, get paid."	On demand, mobile
Crew	DOP, gaffer, AC, runner, etc.	"Accept assignments, read call sheets, get reimbursed."	On demand, mobile

The "THE one job" is the single most important sentence in this PRD — it determines what each portal's landing screen looks like.

! **Open question for Boss:** are these 4 sentences correct? If not, what's the real one-sentence job for each?

5. GOALS & NON-GOALS

Goals (v1 ship target Q3 2026)

- 🌟 **NEW North Star** — *3-second comprehension*: an outsider who has never seen the system can correctly state what each portal is for within 3 seconds of opening it.
- 🔪 **Subtract** — identify and deprecate / progressively-hide ≥ 20 % of features (by count of sidebar items + tabs + buttons).
- ⚡ **Compress** — top-10 highest-frequency tasks have an avg path length of ≤ 3 clicks (down from estimated 5–7).
- 🌀 **Hierarchy** — every main screen has 1 **primary action** + ≤ 3 **secondary actions** above the fold.
- 🗺️ **Preserve** — 4-portal structure (Production · Client · Talent · Crew) stays exactly as today.
- 📱 Talent + Crew portals usable on phone, on-set.
- 🎭 Boss can demo the system to a new client without explaining where things are.

Non-Goals (explicit, v1 will NOT do)

- ❌ Merge or rename portals (director explicitly vetoed)
- ❌ Backend / data-model changes
- ❌ New functional modules
- ❌ Delete features outright without director sign-off (hide first, delete later)
- ❌ Native iOS / Android app (PWA only if scope allows)
- ❌ Multi-tenant, i18n, realtime co-edit

6. SUCCESS METRICS

TIER	METRIC	BASELINE	TARGET (V1)
North Star	3-second comprehension test pass rate (outsider correctly guesses portal purpose)	~30 % (v1 colorful cards)	≥ 90 %
Subtract	Visible feature count per portal	TBD (audit pending)	−20 %
Compress	Avg clicks on top-10 tasks	5.5 (estimated)	≤ 3.0
Quality	Lighthouse mobile (Talent/Crew)	unknown	≥ 90
Quality	Feature regression count	n/a	0
Adoption	Director "would recommend" score	n/a	≥ 9 / 10
Adoption	Talent/Crew weekly logins	unknown	+50 % within 4 weeks of la

! **Open question for Boss:** are the targets realistic, especially −20 % feature deprecation?
Need to align on tolerance.

7. SOLUTION OVERVIEW – DESIGN PHILOSOPHY

Four principles, in priority order:

1. **Subtract before you add.** Every Sprint reviews what to remove before what to build. If we can't justify a feature, it goes behind progressive disclosure first (collapsed by default), then a future Sprint deletes it.
2. **Each portal screams its purpose.** First-time visitor knows in 3 seconds what this portal is for. Implementation: each portal's landing page leads with one declarative headline ("Manage today's productions" / "Review and approve" / "Your next booking" / "Your next assignment") rather than a generic "Dashboard" title.
3. **Status Board, not Action Center.** The director's approved Dashboard demo organises chronologically and by domain — Active Projects table + Activity Feed. We follow that mental model across all 4 portals (each has a Board appropriate to its job).
4. **Brand carries through everything.** Visual tokens (`#D8FF00` brand, `#000` ink, League Gothic display) live in CSS variables. New components consume tokens, not local hex.

See Appendix C for the exhaustive component / token inventory.

11. MILESTONES (NEXT 6 WEEKS)

The compressed plan. Detailed scope per sprint mirrors §1 timeline table.

SPRINT	DATES	DEMO / GATE
Sprint 0	5/20 → 5/28	Live at https://jerry6063.github.io/HXVP-v2-demo/
Sprint 0.5	5/29 → 6/4	End-of-week gate: director signs §12 user flows. No code past this point without sign-off.
Sprint 1 — 6/15 Milestone	6/5 → 6/15	Live demo to director on 6/15: all 4 portals reveal "the one job" within 3 seconds; ⚙️ works; Tier-3 features collapsed.
Sprint 2 — 7/6 Launch	6/16 → 7/6	Production rollout to real users on 7/6 (or earliest weekday). Top user flows in §12 work end-to-end.
Post-launch (v1.5)	7/7+	Deep detail page rollout · Shoot Command Center · Cascade prompts · Bulk ops

Implication: the existing Phase 2 / 3 / 4 / 5 spec in §8 is now **partially post-launch (v1.5+)**. v1 ships with:

- 4 redesigned portal landing pages (the first screen each persona sees)
- ⚙️ search
- The visual system applied to all routable pages' shells (sidebar + header)
- Deep detail pages may retain v1 visual styling internally — acceptable because primary persona's main flows don't visit them daily

This is honest about scope. Director should know what will and won't be polished by launch.

Part II – Detailed Specification (for Engineers)

8. PHASED REQUIREMENTS

PHASE 0 – VISUAL BASELINE DONE

ITEM	STATUS	LOCATION
Brand CSS tokens (<code>--color-brand</code> etc.)		<code>frontend/src/index.css</code>
<code>Button</code> / <code>Input</code> / <code>Card</code> primitives		<code>frontend/src/components/ui/</code>
<code>StatCard</code> / <code>StatusBadge</code> / <code>LoadingSpinner</code> restyled		<code>frontend/src/components/</code>
<code>PortalLayout</code> dark + grouped sidebar		<code>frontend/src/components/PortalLayout.jsx</code>
<code>HomePage</code> skewed portal grid	(but currently shows 3 — needs revert to 4)	<code>frontend/src/components/HomePage.jsx</code>
<code>LoginPage</code> Apple-style entry transition		<code>frontend/src/components/LoginPage.jsx</code> + <code>portalTransition.js</code>
Production Dashboard Status Board		<code>frontend/src/portals/production/Dashboard.jsx</code>
Mock auth (no backend required)		<code>frontend/src/contexts/AuthContext.jsx</code>

PHASE 0.5 – COURSE-CORRECTION (SPRINT 0.5) NEW

ITEM	SPEC	ACCEPTANCE
Revert Model merge — HomePage	3 portal cards → 4 (add Crew back); grid <code>lg:grid-cols-3</code> → <code>lg:grid-cols-4</code> ; "3 Portals" → "4 Roles"	<code>/</code> shows 4 cards; Crew card animates to <code>/crew/login</code> with same Apple-style transition
Revert Model merge — LoginPage	<code>portalMeta.talent.title</code> → "Talent"; <code>portalMeta.crew.title</code> → "Crew"; restore separate subtitles	Crew login page shows "CREW" hero, not "MODEL"
Revert sidebar copy	<code>PortalLayout</code> <code>portalConfigs.talent.title</code> → "Talent"; <code>portalConfigs.crew.title</code> → "Crew"; PORTALS section in production sidebar lists "Client Portal · Talent Portal · Crew Portal" (3 cross-links)	Production admin can jump to all 3 other portals from sidebar
Feature audit doc	Walk each portal's sidebar + each page's tabs + each modal with director; tag each as Essential / Secondary / Deprecate. Output: <code>docs/feature-audit.md</code>	Director signs off on the tags
Portal purpose sentences	One declarative sentence per portal, written by director (or proposed by Jerry and confirmed).	Sentence visible in <code>docs/PRD.md</code> §4 and rendered as login-page subtitle in code

PHASE 1 – HIGHLIGHT WHAT MATTERS (SPRINT 1)

ITEM	SPEC	ACCEPTANCE
Portal landing page hierarchy	Each portal's landing replaces generic "Dashboard" header with: (a) one declarative sentence (the portal's purpose), (b) the one primary CTA / panel, (c) at most 3 secondary panels. Tier-3 (deprecate) features hidden behind a "More" toggle or moved to a Settings page.	3-second comprehension test passes ≥ 90 % with 3 outsiders
Sidebar consolidation	Each section max 5 items visible; Tier-3 items moved to a collapsed "Advanced" subsection or removed	Sidebar visible item count per portal – 20 %
⌘K Global Search	Portal at top-right of every layout; opens overlay; fuzzy matches projects / talent / crew / contracts / invoices / shoots; arrow + Enter navigates	TTI ≤ 200 ms; ≤ 2 keystrokes from any page

PHASE 2 – WORKFLOW COMPRESSION (SPRINT 2)

ITEM	SPEC	ACCEPTANCE
Shoot Command Center	Single <code>/production/shoots/:id</code> page consolidating shoot meta, talent bookings, crew assignments, call sheet generator, production logs, comments. No nested modal trees.	Editing shoot date in this page updates dependents (see cascade)
Cascade Prompts	Changing a shoot date triggers " <i>This will affect N bookings + M assignments. Notify everyone?</i> [Yes / Just this one]"	One click cascade vs current manual 10+ updates
Bulk Actions on Bookings	Multi-select rows + bulk: confirm / decline / re-send call sheet / mark paid	10× speedup on month-end ops
Activity Feed → real data	Replace mock array with API hook; group by day; mobile-friendly	Same data on Dashboard as the events that actually happened

PHASE 3 – VISUAL ROLLOUT (SPRINTS 3–5)

Pages still on v1 visual (≈ 50). Roll out in priority order:

PAGE GROUP	PAGES	SPRINT
Production deep	Projects (list + detail), Talent module, Crew page, Invoices	3
Client	Dashboard, Production timeline, Deliverable center, Talent roster, Invoices	4
Talent	Profile, Bookings, Calendar, Records, Payments, Documents	5
Crew	Profile, Assignments, Calendar, Records, Payments, Documents, Reimbursements	5

Each rolled-out page must:

- Consume only `src/components/ui/*` and the design tokens
- Use `StatusBadge`, `StatCard`, `LoadingSpinner` (already styled)
- Match Dashboard's dark + bordered + League-Gothic-headings pattern
- Visible action count ≤ 4 per main screen

9. INFORMATION ARCHITECTURE (4 PORTALS RESTORED)

```
HXVP Studio v2
|
|— / (Public landing – 4 portal cards)
|   Production · Client · Talent · Crew
|
|— /production (role: production_admin)
|   |— /dashboard      Status Board (Stats + Active Projects + Activity Feed)
|   |— /projects[*]    Productions Module
|   |— /calendar       Shoot Day Tracker
|   |— /talent[*]      Models & Talent
|   |— /crew[*]        Production Crew
|   |— /documents     Documents (call sheets / contracts / checklists / budgets)
|   |— /invoices[*]    Client Payments
|   |— /talent-payments Payroll (Talent + Crew + Time Logs)
|   |— /revenue        Revenue & Expenses
|   |— /messages
|
|— /client (role: client)
|   |— /dashboard, /request, /production, /deliverables,
|   |— /payments, /talent, /messages
|
|— /talent (role: talent)
|   |— /dashboard, /profile, /bookings, /calendar,
|   |— /records, /payments, /documents
|
|— /crew (role: crew)
|   |— /dashboard, /profile, /calendar, /assignments,
|   |— /records, /payments, /reimbursements, /documents
```

Sidebar grouping (consistent across all 4 portals):

```
OVERVIEW → Dashboard · Quick action
WORK      → Work-related nav items with item-count badges (max 5 visible)
PORTALS   → Cross-portal links (production admin → other 3 portals)
FINANCE   → Payments, invoices, payroll (where applicable)
```

10. OUT OF SCOPE (V1)

- Portal merging or renaming (director vetoed)
- Outright feature deletion without director sign-off (hide first, delete in v1.5)
- Backend / API / data-model changes
- New features (AI, smart scheduling, etc.)
- Native mobile apps
- Multi-tenant, i18n, realtime co-edit
- Public marketing site (lives at hxvp.us, not in this scope)

11. RISKS & OPEN QUESTIONS

#	RISK	LIKELIHOOD	IMPACT	MITIGATION
R1	Director's intuition about "non-essential" features ≠ actual user usage data	M	M	Sprint 0.5 audit captures director's tagging; in
R2	"3-second comprehension" target is qualitative and subjective	M	L	Run test with 3 outsiders per portal; documen
R3	Sidebar consolidation may hide a feature the boss actually uses daily	M	M	Each "hide" needs director acknowledgment i
R4	Visual rollout to 50 pages within Sprints 3–5 may slip	H	L	Tagged pages can defer to v1.5 without blocki
R5	Public demo URL may leak competitive info	L	L	Demo data is fake; legacy backend isolated to

Open Questions awaiting Director / Stakeholder decisions

Highest priority — blocks Sprint 1 build:

- **Q1** — §12 flow inventory: for each of the 25 flows F-P / F-C / F-T / F-X, mark ✓ correct · △ partial · X wrong. Add missing flows we forgot. **Sign-off needed by Wed 6/4.**
- **Q2** — §4 portal one-sentence jobs: confirm or rewrite each of the 4 proposed sentences. These literally become the headline copy on each portal's landing page.

Medium priority — needed for Sprint 0.5 audit session:

- **Q3** — §3 — of the three pains (P1 lacks focus / P2 looks complex / P3 unnecessary features), which is **#1** to address first?
- **Q4** — §5 — accept the -20 % feature count target, or prefer aggressive (-40 %) / conservative (-10 %)?
- **Q5** — §7 — can we schedule a 90-minute session with director to walk through every sidebar item and tag each Essential / Secondary / Deprecate? Proposed date: 6/2 or 6/3.

Tactical:

- **Q6** — at 7/6 launch, is mock mode acceptable as a starting state for new users, or must real backend be hooked up day 1?
- **Q7** — Model-merge revert public demo: re-deploy URL the same day as revert (auto via Actions), or wait?

12. USER FLOWS (THE SECTION THE DIRECTOR SHOULD READ MOST CAREFULLY)

! Director sign-off needed by 6/4. For each flow below, please mark: ✓ correct as written · △ partially correct (note what's off) · X wrong or missing (note replacement). The flows you confirm here drive all Sprint 1–2 design and build. **No further engineering past this point happens without confirmation.**

HOW TO READ THE TABLES

COLUMN	WHAT IT MEANS
ID	Stable reference, used in Sprint plans, audit, and tests
Flow	One-sentence user story: "Persona does X so Y"
Trigger	What initiates this flow today
Today (v1)	Approx clicks / pages traversed in current production system
v2 Target	Click goal in redesigned system
Freq	How often persona performs this — D(aily) / W(eekly) / M(onthly)

12.1 PRODUCTION PORTAL FLOWS (STUDIO ADMIN)

Persona's one-sentence job: *"See what's blocking today and unblock it."*

ID	FLOW	TRIGGER	TODAY	V2 TARGET	FREQ
F-P-01	Glance at what's blocked or needs me right now	Login	5+ scroll across Dashboard panels	2 (Status Board surfaces above the fold)	D
F-P-02	Convert a new client request into a project	New Project Request arrives	6: Requests → open → "Create Project" → fill → save → confirm	3 (one-click promote)	W
F-P-03	Plan a new shoot (date · location · requirements)	Project needs shoot	5: Project detail → Shoots tab → "New Shoot" → fill modal → save	3 (inline within Project)	W
F-P-04	Build a talent shortlist + send availability inquiries	Shoot needs talent	8+: Talent module → filter → multi-select → "Send Inquiry" modal → fill → confirm	4 (inline shortlist drawer on Shoot page)	W
F-P-05	Build crew assignment + send availability inquiries	Shoot needs crew	8+: Crew page → similar to F-P-04	4 (mirror of F-P-04)	W
F-P-06	Send call sheet to confirmed people for tomorrow's shoot	Day before shoot	7: Shoot → Call sheets tab → "New" → fill / pre-fill → preview → send	3 (one-click generate from confirmed bookings + assignments)	W
F-P-07	Approve time logs at month end	Month-end	10+ per person (open each log → review → approve)	3 (bulk approve view, deferred to v1.5 — partial in v1)	M
F-P-08	Issue invoice to client	Project milestone reached	6: Invoices → "New" → select project → line items → preview → send	3 (one-click from Project / milestone)	W
F-P-09	Mark invoice as paid + record payment	Client paid	4: Invoice → "Mark paid" → confirm → record	2	W
F-P-10	Move a shoot to a different date and notify everyone	Schedule change	12+ (edit shoot + manually notify each person)	3 (cascade prompt — partial in v1, full in v1.5)	W

12.2 CLIENT PORTAL FLOWS

Persona's one-sentence job: *"Check my project and approve what needs approving."*

ID	FLOW	TRIGGER	TODAY	V2 TARGET	FREQ
F-C-01	Submit a new project request	Need shoot	5: Login → New Request → fill → upload refs → submit	3	M
F-C-02	Check progress of my active project	Curious / due-date approaching	4: Login → Production → my project → scroll	2 (Dashboard surfaces it)	W
F-C-03	Review and approve deliverables	Deliverables ready	6: Login → Deliverables → open shoot folder → review each → approve each	3 (inline approve, grid view)	W
F-C-04	Sign a contract	Contract sent	5: Login → Notifications → contract → review → sign	3	M
F-C-05	Pay an invoice	Invoice received	4: Login → Payments → invoice → pay	3	M

12.3 TALENT PORTAL FLOWS (MODEL · ACTOR · CAST)

Persona's one-sentence job: *"Accept bookings, read call sheets, get paid."*

ID	FLOW	TRIGGER	TODAY	V2 TARGET	FREQ
F-T-01	Respond to availability inquiry (Accept / Decline)	Inquiry pushed	4 (web): Login → Bookings → inquiry → respond. On mobile: even more	1 tap (mobile-first home card with inline Accept / Decline)	W
F-T-02	Read tomorrow's call sheet (location · time · wardrobe)	Day before shoot	4: Login → Bookings → upcoming → call sheet	1 (home shows next call sheet at top)	W
F-T-03	Update profile / availability calendar	Schedule change	6: Profile → calendar → click date → mark → save	3	M
F-T-04	Submit time log after a shoot	Wrap	5: Login → Records → log → fill → submit	2 (one-tap from shoot detail)	W
F-T-05	Check earnings / payment status	Payday curiosity	3: Login → Payments → view	2 (home shows next payout)	W

12.4 CREW PORTAL FLOWS (DP · GAFFER · AC · RUNNER ETC.)

Persona's one-sentence job: *"Accept assignments, read call sheets, get reimbursed."*

ID	FLOW	TRIGGER	TODAY	V2 TARGET	FREQ
F-X-01	Respond to availability inquiry	Inquiry pushed	4 (web), worse on mobile	1 tap mobile	W
F-X-02	Read tomorrow's call sheet	Day before shoot	4	1	W
F-X-03	Submit time log after a shoot	Wrap	5	2	W
F-X-04	Submit a reimbursement (gas · meals · gear rental)	Expense incurred	6: Reimbursements → New → fill → upload receipt → save → submit	3 (mobile-friendly photo upload)	W
F-X-05	Check earnings / payment status	Payday curiosity	3	2	W


Notes for director review

- Frequencies (D/W/M) are best-guesses — please correct any that feel wrong.
- "Today" click counts are estimates; actual numbers will be measured during Sprint 0.5 audit.
- Many "v2 Target = 1 tap" flows for Talent / Crew depend on the **mobile-first home redesign** in Sprint 2.

13. WORKFLOWS (MULTI-STEP PROCESSES SPANNING MULTIPLE SESSIONS OR PERSONAS)

These are end-to-end business processes that string the §12 flows together. v2 doesn't change the workflow shapes — only how smoothly each step connects.


W-1 · PROJECT LIFECYCLE (CLIENT REQUEST → INVOICE PAID)

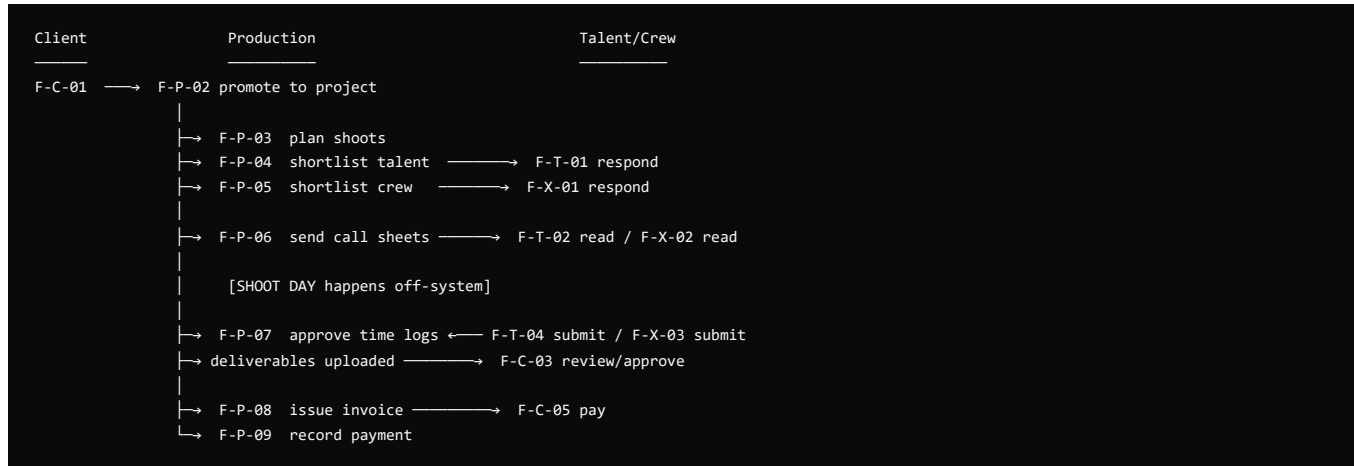

v2 stress points (where boss reported most friction):


- F-P-04 / F-P-05 (shortlist + inquiries) — currently 8+ clicks each, the most expensive step
- F-P-06 (call sheets) — should auto-fill from confirmed bookings, not require re-typing
- F-P-10 (date change) — currently zero cascade, manual re-notify chain

W-2 · SHOOT DAY LIFECYCLE (PLAN → WRAP → SETTLE)



v2 simplification: the entire shoot day flow ideally collapses into a single Shoot Command Center page (planned v1.5) — but for launch, T-7 → T+1 should at least feel like a coherent vertical narrative inside the Project page, not 7 disconnected pages.

W-3 · TALENT / CREW ONBOARDING



v2: profile completeness % progress bar on home so models know what's left.

W-4 · MONTH-END PAYROLL

```
1st of month  F-P-07 admin reviews all time logs of prior month
              ↓
              bulk approve where possible (v1.5 capability)
              ↓
              talent/crew payments queued
              ↓
              F-T-05 / F-X-05 see "paid" status update
```

v2 stress point: 30+ time logs per month per studio is currently 30 × ~5 clicks = 150+ clicks.
Bulk operations (v1.5) are critical here, but partial bulk in v1 acceptable.

Appendix A – Glossary

TERM	DEFINITION
Portal	One of four top-level role-based UI shells: Production, Client, Talent, Crew
Shoot	A single day of filming/photographing, belongs to a Project
Call Sheet	Document sent to talent + crew the day before a shoot with location, call time, wardrobe
Booking	A talent's confirmed participation in a Shoot
Assignment	A crew member's confirmed participation in a Shoot
Time Log	Hourly record submitted by talent/crew for payment
Feature tag	Essential (always-visible) · Secondary (one-click reveal) · Deprecate (hidden / removed)
DRI	Directly Responsible Individual (Apple PM convention)
3-second comprehension	Outsider correctly states portal purpose within 3 seconds of opening

Appendix B – References

- Public brand site (visual reference): <https://hxvp.us/>
- SetHero (functional reference for call-sheet workflow): <https://sethero.com/>
- Director-approved Dashboard demo screenshot: see Sprint 0 commit `ad6ad68`
- Director feedback screenshot (2026-05-28, v1 main 4-portal grid): attached to chat
- Original engineer's deploy (legacy v1): <https://hxvp-studio-frontend.onrender.com/production>
- v2 public demo: <https://jerry6063.github.io/HXVP-v2-demo/>

Appendix C – Component & Token Inventory

DESIGN TOKENS (CSS VARIABLES, DEFINED IN FRONTEND/SRC/INDEX.CSS)

--color-brand	#D8FF00	electric lime (primary CTA / accent)
--color-brand-hover	#C2E600	
--color-accent-2	#F0523D	coral (secondary / warning)
--color-ink	#000000	primary text
--color-ink-soft	#272727	
--color-ink-muted	#737373	
--color-ink-subtle	#A9A9A9	
--color-paper	#FFFFFF	
--color-paper-soft	#FAFAFA	
--color-paper-dark	#0A0A0A	main app background
--color-rule	#E7E7E7	
--font-display	"League Gothic"	(uppercase, condensed, large)
--font-sans	"Helvetica Neue" / Helvetica / Arial	
--radius-card	2px	(editorial – almost no rounding)

UI PRIMITIVES (FRONTEND/SRC/COMPONENTS/UI/)

COMPONENT	VARIANTS	SIZES
Button	primary · secondary · ghost · danger	sm · md · lg
Input	input · textarea · select (via as prop)	—
Card	default · paper · emphasis (+ Card.Header / .Body / .Footer)	—

STATEFUL COMPONENTS (PRESERVE EXISTING API, RESTYLED)

COMPONENT	NOTE
StatCard	color prop accepts legacy indigo/emerald/amber/sky for back-compat, all map to brand yellow
StatusBadge	40+ legacy statuses bucketed into 5 semantic tones (success · warning · info · danger · neutral) tuned for light backgrounds
LoadingSpinner	Yellow ring on dark backgrounds

TRANSITION UTILITIES

frontend/src/components/portalTransition.js — shared motion config:

- PORTAL_TRANSITION — 800 ms ease-in-out-quart for layoutId-driven cross-page morph
- portalLayoutId(key) — naming factory keeping HomePage and LoginPage in sync

Appendix D – Proposed Top-10 Tasks (for click-count + comprehension baselines)

1. View today's pending bookings (Production admin)
2. Send a call sheet for tomorrow's shoot
3. Approve a Time Log
4. Issue an invoice
5. Mark an invoice paid
6. Move a shoot to a different date (incl. notifications)
7. Add a new model to the roster
8. Client approves a deliverable
9. Client signs a contract
10. Talent / Crew accepts a booking on mobile

Appendix E – File Inventory & LOC

(Generated 2026-05-28 from `v2-redesign` branch.)

GROUP	FILES	LOC
Total <code>frontend/src/**/*.jsx</code>	74	26 712
<code>portals/production/**</code>	27	13 350
<code>portals/client/**</code>	7	2 320
<code>portals/talent/**</code>	8	2 985
<code>portals/crew/**</code>	8	2 690
<code>components/**</code> (shared)	17	2 900
<code>api/**</code> (hooks + client)	2	1 950

Pages over 500 LOC ("heavy detail pages") are listed in `appendix-e-detail.md` (TBD) — these are high-priority Sprint 3 targets.

Appendix F NEW – Feature Audit Framework

The Sprint 0.5 audit answers the question: *for every feature in the system, is it Essential, Secondary, or Deprecate?*

TAGGING RUBRIC

TAG	CRITERIA	UI IMPLICATION
● Essential	(a) Used $\geq$ once per day by primary persona, OR (b) blocks a core workflow if missing	Always visible, top of sidebar / page hierarchy
● Secondary	(a) Used 1–4 $\times$ per month, OR (b) used by a small subset of users daily, OR (c) supporting/admin function	Hidden behind one click (e.g. "Advanced" section, settings menu, contextual modal)
● Deprecate	(a) Used $<$ 1 $\times$ /month by anyone, OR (b) overlaps with another feature that's better, OR (c) director explicitly says "I never use this"	Removed from sidebar in v1; soft-hidden in code (kept routable for transition); deleted in v1.5

AUDIT PROCESS (SPRINT 0.5)

- Inventory** (Jerry, 1 day before director meeting): generate a flat list of every sidebar item, every page tab, every modal action across the 4 portals. Format: `docs/feature-audit.md` with rows = features, columns = [Portal · Path · Description · Tag · Director note].
- Walkthrough** (Director + Jerry, 90 min session): step through the list, director tags each row. Where unclear, log in "Director note" column for follow-up.
- Decision** (Jerry, same day): close the list, commit `docs/feature-audit.md`.
- Apply** (Sprint 1): UI changes per the rubric above. No feature is *deleted* in Sprint 1 — only hidden / collapsed.
- Instrument** (Sprint 1 onward): add usage analytics on deprecated features. If anything unexpectedly used $>$ 1 $\times$ /month for 4 weeks, promote it back to Secondary.
- Delete** (v1.5, post-launch): items still cold after 4 weeks of instrumentation get deleted from code.

EXAMPLE AUDIT ROW FORMAT

Portal	Path	Feature	Tag	Note
Production	/production/messages	In-app messaging	Secondary	"Most ppl use WeChat, but useful log"
Production	/production/revenue	Revenue analysis charts	Essential	"I look at this every Monday"
Production	/production/talent-payments	Stripe payout integration	Secondary	"Used 2-3x/month at month-end"
Client	/client/talent	Talent roster sharing	Deprecate	"Client never logs in to see this"

CHANGE LOG

VERSION	DATE	AUTHOR	NOTES
0.1	2026-05-28	Jerry Zheng	Initial draft post-Sprint 0; assumed Talent+Crew merge into Model
0.2	2026-05-28	Jerry Zheng	Director feedback received. Reverted Model merge (4 portals stay). Reframed problem from "too many clicks" to
0.3	2026-05-28	Jerry Zheng	Deadlines locked: 6/15 internal + early-July launch. Compressed roadmap from 6 sprints to 2 + 0.5 prep. Added

Next action (boss): read §1 → §12 (the flows tables) → §11. Mark each flow ✓ ⚠ X by 6/4. Once §12 lands and Q1–Q5 are answered, Sprint 0.5 spec freezes and Sprint 1 build begins 6/5.
